

**The Tchuma Tchato Project, in Partnership with Kingdom Life Worship Community Centre/New Hope Pre-School. Report on the setting up of gated fence.**

**O Projecto Tchuma Tchato, em Parceria com Kingdom Life Worship Community Centre/ Pré-Escola Nova Esperança. Relatório sobre a montagem da vedação com portões.**

**2020.01.24 (Day 01)**

Orlando showed up around 09:00 with two other guys. They started digging the holes on one side of the property. Orlando is very much in and out I'm told he is finishing up another job close by. I went around getting the cement and poles. Also got 500m wire and went with Pastor Jabu to order the concrete. They were supposed to set up the poles on the side but that never happened. I hope Orlando finishes the other job quick so he can focus on this one. Next working day will be monday. Prayers are that it doesn't rain too much that the holes don't wash away and that the school kids stop playing throwing the dirt back in the holes...



**2020.01.24 (Dia 01)**

O Orlando apareceu por volta das 09:00 com mais duas pessoas. Começaram a cavar os buracos num dos lados da propriedade. O Orlando vai e vem, dizem-me que está a terminar outra obra perto. Fui buscar o cimento e os postes. Também consegui 500m de arame e fui com o Pastor Jabu encomendar a argamassa. Era para colocar os postes num dos lados mas isso não aconteceu. Espero que o Orlando termine a outra obra depressa e se dedique a esta. Segunda-Feira será o próximo dia de trabalho. Oramos que não chova em demasia, para que os buracos não desapareçam e que os garotos de escola não atirem terra para dentro deles...

**2020.01.27 (Day 02)**

Orlando is having hard time showing up at 07:30. Today Orlando, Quinito and another guy were able to set the poles on one side. I got the 2 poles that were left at CashBuilders and later got 4 more at Obaro, so they could finish. Also got 4 stays, one bag of cement which makes three, and one double gate at Mica but they gave us two of the same side. Need to go by tomorrow and let them know to give us two of the other side since we need two double gates. The rest of the poles at CashBuilders are only going to arrive Wednesday or Thursday so tomorrow there's no job. Took some more pictures.



**2020.01.27 (Dia 02)**

O Orlando está a ter dificuldade em chegar às 07:30. Hoje o Orlando, o Quinito e outra pessoa conseguiram colocar os postes num lado. Trouxe os 2 postes que estavam no Cash Builders e consegui 4 mais tarde no Obaro, para que pudessem terminar. Também consegui 4 suportes, um saco de cimento o que perfaz três, e uma cancela no Mica mas deram duas metades do mesmo lado. Tenho que voltar lá amanhã e dizer-lhes para nos darem duas metades do mesmo lado da próxima vez. O resto dos postes no CashBuilders só vão chegar Quarta ou Quinta-Feira por isso amanhã não há obra. Tirei algumas fotos.

**2020.01.29 (Day 03)**

Was by Mica yesterday to talk about the gate and paid for another one. Today went to get the one sided gate to bring back to Mica so they could give me 2 sets of the right gates. Took pictures. Went by CashBuilders but the poles haven't arrived yet.



**2020.01.29 (Dia 03)**

Passei pela Mica ontem para falar sobre as meias cancelas e paguei mais um par. Hoje fui à obra buscar as meias cancelas para as devolver e me pudessem dar duas com as metades a condizer. Tirei fotos. Fui ao Cash Builders mas os postes ainda não chegaram.

**2020.02.02**

Took a fall and broke ribs. A 6 week projection to recuperate A blessing in disguise because...

**2020.02.02**

Caí e fracturei costelas. Calcula-se 6 semanas para a recuperação. Uma bênção disfarçada porque...

**2020.02.03**

This day the protests and riots started in Barberton and mainly at the location where the church is located, making it hard



**2020.02.03**

Hoje começaram os protestos e os tumultos em Barberton, principalmente na área onde está situada a igreja, o que dificulta



for the work to continue. Roads blocked, trucks and cars set on fire, looting, people being shot and killed, mayhem.

### **2020.03.10 (Day 04)**

Some law and order has come to the town. Was able to go by the church/pre-school to deliver 13 corner posts. Hopefully we'll resume work tomorrow.

### **2020.03.12 (Day 05)**

Met Orlando and the other guy at 11:15. They're going to setup the 13 poles they have there and he asked me to bring 2 more bags of cement after lunch at 15:00. Went there and stayed until 18:30. Orlando and the other guy put up the gate posts. Took pictures.

### **2020.03.13 (Day 06)**

Went by the site. Orlando and the other guy (need to get his name) were there preparing the ground for the poles at the back. Orlando says the other guy will be coming over tomorrow Saturday to weed out the ground and then Monday they'll start fitting the supporting wire. He figures by Wednesday they can start fitting the wire fence (mesh).

### **2020.03.16 (Day 07)**

Went by the site. Martin (the other guy's name) is there to weed out the grass around the fence. He doesn't know if Orlando is coming by today or not but he's pretty sure not tomorrow. Went by Mica and paid for the mesh.

### **2020.03.17 (Day 08)**

Went by the site to deliver the mesh with the trailer. Martin is there weeding out the grass. Told me they need 7 more stay poles. Orlando maybe coming later... Took pictures. Went by Cash Builders, got the stays and went back to deliver them. Took a picture more.

### **2020.03.18 (Day 09)**

Went by the site around 09:30. Orlando and Martin haven't arrived yet. Took some pictures. Then they arrived and Orlando noticed one of the stays is missing. Need to get another one. Got another one but it so happens Pastor Jabu had put it aside but one more was needed anyway. The mesh is too high, needs to be 1.5m instead of 1.8. Need to go by Mica tomorrow and try to change it. Also need thin wire to secure the thick wire to the poles. Orlando



continuarmos a obra. As ruas fechadas, caminhões e carros a arder, pilhagem, pessoas a serem mortas a tiro, o caos.

### **2020.03.10 (Dia 04)**

Alguma lei e ordem chegou à cidade. Consegui passar pela igreja/pré-escola e entregar os 13 postes. Se Deus quiser recomeçaremos os trabalhos amanhã.

### **2020.03.12 (Dia 05)**

Encontrei com o Orlando e a outra pessoa às 11:15. Vão começar a colocar os 13 postes que estão lá e pediu-me para trazer mais 2 sacos de cimento depois do almoço às 15:00. Fui lá e fiquei até às 18:30. O Orlando e a outra pessoa colocaram os postes. Tirei fotos.

### **2020.03.13 (Dia 06)**

Passei pela obra. O Orlando e a outra pessoa (tenho que lhe perguntar o nome) estavam lá nas traseiras, a preparar o chão para os postes. O Orlando diz que a outra pessoa virá amanhã Sábado para limpar o chão das ervas e que Segunda-Feira vão começar a montar o arame. Ele acha que Quarta-Feira poderão começar a colocar a rede.

### **2020.03.16 (Dia 07)**

Passei pela obra. O Martin (é o nome da outra pessoa) está lá a cortar a erva no caminho da vedação. Ele não sabe se o Orlando vem hoje ou não mas com certeza não virá amanhã. Passei pela Mica e paguei a rede.

### **2020.03.17 (Dia 08)**

Passei pela obra com o atrelado para entregar a rede. O Martin está lá a cortar a erva. Disse que são necessários mais 7 suportes. O Orlando talvez venha mais tarde... Tirei fotos. Passei pelo Cash Builders, consegui os suportes e fui entregá-los. Tirei mais uma foto.

### **2020.03.18 (Dia 09)**

Passei pela obra cerca das 09:30. O Orlando e o Martin ainda não chegaram. Tirei algumas fotos. Entretanto chegaram e o Orlando viu um dos postes a faltar. É preciso outro. Afinal o Pastor Jabu tinha-o tirado porque estava solto mas é preciso mais um mesmo assim. A rede é alta demais, tem que ser 1,5m em vez de 1,8m. Tenho que passar pela Mica amanhã e tentar trocá-la. Também é preciso arame fino para prender o arame grosso aos



and Martin were busy stretching the thick wire. Took photos.

### 2020.03.19 (Day 10)

Pass by Mica, see about exchanging the mesh and get the 2mm wire. Go get the mesh at the church and bring it to Mica to exchange. Go back to the church with the 1.2m mesh and offload it. Orlando and Martin showed up. In the afternoon around 16:00 went by the site again. The mesh is too short now. An idea is to complement the height with razor wire. Took pictures.

### 2020.03.20 (Day 11)

Went out to Mica and Obaro (Cash Builders don't have) to quote price for the razor concertina wire. Mica is 10m x 0.5m, R189.00, Obaro is 15m x 0.5m, R216.00. Went by the site, measured the perimeter again and is now 120.6m. I think we'll have one roll of mesh extra. Orlando and Martin are busy fitting the mesh. Took pictures. Went back to the site in the afternoon around 16:00. The Pastor is not back. Talked to Orlando, I think we just gonna get more of the mesh, cut it in half and complete the height. Took more pictures.

### 2020.03.21 (Day 12)


I was going to pass by the site but didn't. Martin was there fitting wire.

### 2020.03.23 (Day 13)

Went by the site in the morning. Orlando and Martin are there working on the back of the church. Orlando tells me he thinks there's gonna be half roll of mesh left over. Took pictures.

### 2020.03.24 (Day 14)

Went by the site in the morning, after getting one roll of mesh and the wire. Waited for Orlando and Martin to arrive and then he tells me he needs another roll and the wire is too thick. Went back to Mica to get another roll of mesh and change the wire and go back to the site to deliver it. Took some pictures. In the afternoon went back to the site around 15:30 and stayed there until 17:30. The guys fitted the gates and finished securing the mesh to the wire.

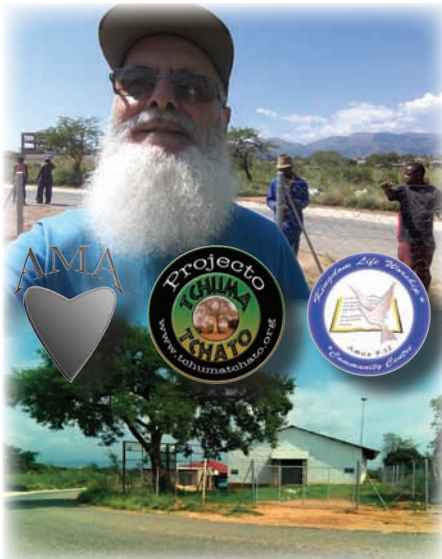

postes. O Orlando e o Martin estavam a esticar o arame grosso. Tirei fotos.

### 2020.03.19 (Dia 10)

Passei pela Mica, para ver sobre trocar a rede e conseguir o arame de 2mm. Ir buscar a rede à igreja e trazê-la de volta à Mica para trocar. Voltar à igreja para a descarregar. O Orlando e o Martin apareceram. À tarde, por volta das 16:00, passei pela obra. Agora a rede é curta demais. Uma ideia é acrescentar na altura com arame farpado tipo acordeão. Tirei fotos.

### 2020.03.20 (Dia 11)

Fui à Mica e ao Obaro (o Cash Builders não tem) para saber o preço do arame farpado acordeão. Na Mica são 10m x 0,5m, R189.00 (€10,13), no Obaro 15m x 0,5m, R216.00 (€11,58). Voltei à obra, medi o perímetro novamente e são agora 120,6m. Acho que vai sobrar um rolo de rede. O Orlando e o Martin estão ocupados a colocar a rede. Tirei fotos. Voltei à obra à tarde cerca das 16:00. O Pastor ainda não voltou. Falei com O Orlando, acho que vamos conseguir mais rede, cortá-la ao meio no comprimento e acrescentar na altura. Tirei mais fotos.

### 2020.03.21 (Dia 12)

À passar na obra mas não passei. O Martin esteve lá a colocar o arame.

### 2020.03.23 (Dia 13)

Passei pela obra na parte da manhã. O Orlando e o Martin estão lá a trabalhar nas traseiras da igreja. O Orlando diz-me que pensa que irá sobrar um rolo de rede. Tirei fotos.

### 2020.03.24 (Dia 14)

Passei pela obra de manhã, depois de conseguir um rolo de rede e o arame. Esperei pelo Orlando e o Martin chegarem e então ele diz-me que precisa de mais um rolo e que o arame é grosso demais. Voltei à Mica para conseguir mais um rolo de rede e trocar o arame e voltei à obra para os entregar. Tirei algumas fotos. De tarde votei à obra cerca das 15:30 e fiquei por lá até às 17:30. Os dois montaram os portões e terminaram de amarrar a rede ao arame grosso.
